

AD-A064 127

RCA CORP LANCASTER PA SSD-ELECTRO-OPTICS AND DEVICES  
MANUFACTURING METHODS AND TECHNOLOGY (MM AND T) MEASURE FOR FAB--ETC(U)  
JUL 78 B B ADAMS, S W KESSLER, R E REED

F/6 9/1

DAAB07-76-C-8120

NL

UNCLASSIFIED

| OF |

AD  
A064127



END  
DATE  
FILMED  
4-79  
DDC



DDC FILE COPY

ADA064127

Eighth Quarterly Progress Report

MANUFACTURING METHODS AND TECHNOLOGY (MM&T)  
MEASURE FOR FABRICATION OF SILICON TRANSCALANT THYRISTOR

Period Covered:

1 July 1978 to 30 September 1978  
Contract No. DAAB07-76-C-8120


Placed by:

U. S. Army Electronics Command  
Production Division  
Production Integration Branch  
Fort Monmouth, New Jersey 07703

Contractor:

RCA Corporation  
SSD-Electro-Optics & Devices  
New Holland Avenue  
Lancaster, Pennsylvania 17604

Approved for public release; distribution unlimited



79 01 25 027

#### DISCLAIMER STATEMENT

The findings in this report are not to be construed as an official Department of the Army position unless so designated by other authorized documents.

#### DISPOSITION INSTRUCTIONS

Destroy this report when it is no longer needed. Do not return it to the originator.

#### ACKNOWLEDGEMENT STATEMENT

This project has been accomplished as part of the U.S. Army (Manufacturing and Technology) Program, which has as its objective the timely establishment of manufacturing processes, techniques or equipment to insure the efficient production of current or future defense programs.



**MANUFACTURING METHODS AND TECHNOLOGY (MM&T)  
MEASURE FOR FABRICATION OF SILICON TRANSCALENT THYRISTOR**

**Eighth Quarterly Progress Report**

**Period Covered: 1 July 1978 to 30 September 1978**

**Object of Study: The objective of this manufacturing methods and technology measure is to establish the technology and capability to fabricate Silicon Transcalent Thyristors.**

**Contract No. DAAB07-76-C-8120**

**Approved for public release; distribution unlimited**

**Prepared by:  
B. B. Adams  
S. W. Kessler  
R. E. Reed  
D. R. Trout**

79 01 25 027

Unclassified

SECURITY CLASSIFICATION OF THIS PAGE (When Data Entered)

REPORT DOCUMENTATION PAGE		READ INSTRUCTIONS BEFORE COMPLETING FORM
1. REPORT NUMBER Eighth Quarterly Progress Report	2. GOVT ACCESSION NO.	3. RECIPIENT'S CATALOG NUMBER
4. TITLE (and Subtitle) Manufacturing Methods and Technology (MM&T) Measure for Fabrication of Silicon Transcendent Thyristor		5. TYPE OF REPORT & PERIOD COVERED Quarterly Report 1 July 1978 to 30 Sep. 1978
7. AUTHOR(s) B. B. Adams S. W. Kessler R. E. Reed D. R. Trout		6. PERFORMING ORG. REPORT NUMBER
9. PERFORMING ORGANIZATION NAME AND ADDRESS RCA Corp., SSD-Electro Optics & Devices New Holland Avenue Lancaster, PA 17604		8. CONTRACT OR GRANT NUMBER(s)  DAAB07-76-C-8120
11. CONTROLLING OFFICE NAME AND ADDRESS U.S. Army Electronics Command Production Div., Prod. Integration Branch Ft. Monmouth, NJ 07703		10. PROGRAM ELEMENT, PROJECT, TASK AREA & WORK UNIT NUMBERS  Project No. 2769732
14. MONITORING AGENCY NAME & ADDRESS (if different from Controlling Office)		12. REPORT DATE July, 1978
		13. NUMBER OF PAGES 53
		15. SECURITY CLASS. (of this report)  Unclassified
		15a. DECLASSIFICATION/DOWNGRADING SCHEDULE
16. DISTRIBUTION STATEMENT (of this Report)  Approved for public release; distribution unlimited, except that the information presented is not to be construed as a license to manufacture or sell the device described without permission.		
17. DISTRIBUTION STATEMENT (of the abstract entered in Block 20, if different from Report)		
18. SUPPLEMENTARY NOTES		
19. KEY WORDS (Continue on reverse side if necessary and identify by block number)  Thyristor                      Power Switching Component                      Transcendent Thyristor High Current SCR              Power Conditioning Component                      Production Engineering Heat-Pipe Cooling              Solid State Device                      Electrical Testing of SCR		
20. ABSTRACT (Continue on reverse side if necessary and identify by block number)  ➤ This Eighth and Final Quarterly Report describes the conclusion of the MM&TE program for the Transcendent (Heat-Pipe cooled) thyristors. Production engineering measures for the device have been concluded. Test results on the 40 pilot production samples are listed.		

DD FORM 1 JAN 73 1473

EDITION OF 1 NOV 65 IS OBSOLETE

Unclassified

SECURITY CLASSIFICATION OF THIS PAGE (When Data Entered)

Unclassified

SECURITY CLASSIFICATION OF THIS PAGE(When Data Entered)

20. (Continued)

The present status includes the successful completion of the pilot production rate demonstration in accordance with the Preliminary Pilot Run Report as well as the completion of the fabrication of all of the pilot production devices and their shipment to the government.

Plans for the next Period include the completion of the documentation requirements which include the final monthly reports, this final quarterly report, the final technical report and the general report on Step II.

Unclassified

SECURITY CLASSIFICATION OF THIS PAGE(When Data Entered)

# ABSTRACT

This Eighth Quarterly Technical Report on the MM&TE Contract DAAB07-76-C-8120 for Transcalent (Heat-Pipe cooled) SCR Thyristors describes the progress on device production for the 40 Pilot Run Samples. Also described are the problems encountered and the results achieved in the testing of the numerous characteristics, including the sampling of some design and environmental parameters as required by the contract.

Actual test results for the Pilot Run Samples are included to verify that the device design can be successfully reproduced to conform to the electrical, mechanical and thermal specification of SCS-477. Production rate data was prepared for the production rate demonstration and included in the Preliminary Pilot Run Report, issued separately.

The latest revision to the PERT Chart, prepared and submitted on 29 August 1977, continued to be applicable as the balance of the work program remained on schedule. All of the Pilot Run has been completed and the devices delivered to the government.

Plans for the next period include the completion of the documentation requirements for both Steps I and II.

ACCESSION BY	
NYIS	<input checked="" type="checkbox"/>
DDC	<input type="checkbox"/>
UNCLASSIFIED	<input type="checkbox"/>
RESTRICTED	<input type="checkbox"/>
BY	
DATE	
FILE	
A	

# TABLE OF CONTENTS

Description	Page No.
DD Form 1473	--
Title Page	1
Abstract	3
Table of Contents	5
List of Illustrations and Tables	7
Purpose	9
Glossary	11
Narrative and Data	13
1. Device	13
a. Description of the Structure	13
b,c. Problem Areas and Work Performed	13
(1) Conversion of Design for Production	13
d. Conclusions	17
e. Drawings	17
2. Process, Equipment and Tooling	18
a. Purpose of Each Step	18
(1) Device Processing and Tooling	18
(2) Electrical and Environmental Test Equipment	18
b,c. Problem Areas and Work Performed	18
(1) Device Processing and Tooling	18
(2) Electrical, Thermal and Environmental Test Equipment	19
d. Conclusions	19
e. Drawings and Photographs	19
3. Flow Chart of Manufacturing Process Yield	20
4. Equipment and Tooling Costs	20

PRECEDING PAGE BLANK-NOT FILMED



# TABLE OF CONTENTS (Continued)

<u>Description</u>	<u>Page No.</u>
5. Data and Analysis	22
a. Inspections	22
(1) Pilot Run Devices	22
b. Discussion of Inspection Results	23
(1) Visual and Mechanical Inspections	23
c. Corrective Action	33
6. Specification	35
7. Requirement for Pilot Run	35
8. Total Cost for Pilot Run	35
9. Program Review	35
Conclusions	37
Program for the Next Period	38
Identification of Personnel	39
Distribution List	43

LIST OF ILLUSTRATIONS AND TABLES

<u>Number</u>	<u>Title</u>	<u>Page No.</u>
	<u>Figures</u>	
1	Flow Diagram for the Transcendent Thyristor Assembly	15
	<u>Tables</u>	
1a,b,c	Summary of Pilot Run Devices Performance vs. Specifications	24
2	Schedule of Prior Technical Achievements Reported Under Contract	49

## PURPOSE

The purpose of this production engineering contract was to establish the technology and capability to fabricate heat-pipe cooled semiconductor power devices, silicon Transcendent Thyristors, Type J15371. The subsequent pilot production of these devices was a part of the contract. This report covers the efforts performed by the contractor in the eighth quarterly period to perform the Pilot Run Sample Device production. Both the engineering and confirmatory samples were adequately characterized previously. Plans for future work are also presented and other pertinent information is further discussed to help assure that the purpose of the contract was accomplished.

This contractual MM&TE program was used to establish the production techniques, to establish the quality control procedures and to verify a pilot production rate capability for the J15371 thyristor, conforming to the drawing attached to AMENDMENT 1 of SCS-477 as well as to the modifications No. P00001, P00002 and P00003 to the contract. Electrical, mechanical, thermal and environmental inspections were a part of the program as well as extensive documentation requirements, per DD 1423.

No high volume production facilities existed at the start of this contract for the Transcendent type of solid-state power device. However, facilitation was accomplished for the pilot rate requirement and higher volume production planning constitutes Step II of the contract. Thus, the time required to produce future large quantities of the J15371 will be reduced for either current military requirements or for future emergency requirements. Reduction of the reproductive costs for production quantities was also accomplished.

The J15371 thyristor is a 400 amperes RMS, 800 volts, forced air cooled solid-state power control device, lighter weight and smaller size than the conventional devices with their externally attached heat-sinks. Ruggedness and improved reliability resulted from these innovations. A blocking voltage capability of 800 volts minimum at 125° Celsius was successful as a requirement. Original R&D efforts were conducted successfully by RCA under Contract No. DAAK02-69-C-0609, for MERADCOM, Ft. Belvoir, VA. Potential applications include power conditioning, power switching, phase control, voltage variable power supply, motor speed control and other high power military equipments.

PRECEDING PAGE BLANK-NOT FILMED



## GLOSSARY

All abbreviations, symbols and terms used in this report are consistent with the Electronics Command Technical Requirements SCS-477, dated 5 December, 1974. This Technical Requirements document, in turn, references MIL-S-19500 for the abbreviations and symbols used therein except, as follows:

VGR = Reverse Gate Voltage

IGR = Reverse Gate Current

The format used for this report is that specified in the DD 1423, namely, ECIPPR No. 15, Appendix C, augmented by MIL-STD-847A. Sub-section numbering is based on Appendix C and the applicable test methods are those referenced in the following military standards:

MIL-STD-750B

MIL-Std-202E

Detail, individual item requirements shall be in accordance with MIL-S-19500.

## NARRATIVE AND DATA

### 1. Device

- a. Description of the Structure - Refer to pages 9-13 of the First Quarterly Report for a description of the Transcalent thyristor device, the applicable reports, and the applicable patents as well as the advantages of this heat-pipe cooled technical approach. Refer to Figure 1 in the Second Quarterly Report for the cross-section drawing of the J15371 with the external dimensions added.
- b,c. Defining the Problem Areas and Work Performed to Resolve the Problem

#### (1) Conversion of Design for Production

The Transcalent Thyristor design achieved under R&D Contract No. DAAK02-69-C-0609 was described in the FTR, October, 1972. Subsequent refinements have been incorporated under Contract N62269-73-C-0635 and by RCA funded engineering projects. Additional engineering has been applied under this MM&TE program to convert the design to one more suitable for production, as described in prior Quarterly Reports covering the period 27 September 1976 to 30 June 1978 and below for the most recent quarterly period.

#### (a) Item No. 0001AC Pilot Run Phase

##### i. SCR Device Fabrication

The remaining Pilot Run samples were fabricated during this quarterly report period. All have passed the 100% basic electrical tests of Table I, Group A in SCS-477 as well as the sampling required for the Table II and III thermal and environmental tests. Refer to Section 5 of this report for a summary of the test results.

This group of Pilot Run devices was shipped in late September, 1978 to complete the contract requirement of 40 deliverable devices. Some of these devices were used to demonstrate the production rate, as required by Section F49 of Part II of the contract.

ii. Pilot Run Production Rate Demonstration

A Pilot Run production rate demonstration was performed on 10 and 11 July at the contractor's Lancaster, PA, location. The Preliminary Pilot Run Report for Fabrication of Silicon Transcendent Thyristor (30 May 1978) was used as a guide for the demonstration.

The aforementioned report described heat-pipe and thyristor device assembly in great detail. Dr. Russell Eaton, III of Ft. Belvoir, VA, witnessed each of the ten steps indicated on page 7 of the report, (Fig. 1 in this report), which shows the flow diagram for device assembly, and found the steps adequate for the production rate goal.

All production assembly steps except one, were performed at the required rate or better. The exception to the required production rate involved the exhaust processing. The six port exhaust facility used has been proven in previous processing of units. However, the six port facility can only produce 4.6 units in an eight hour shift. The capacity per port was 0.8 unit per eight hour day.


Modifying the facility to a 14 port manifold would increase the capacity to eleven units in an eight hour day. The fourteen port system was not available during the pilot run demonstration, however, it is part of the contractor's future plans for high volume production.

A flow diagram for the RCA proprietary J15371 thyristor wafer metallizing, contouring and pretesting was shown in the Preliminary Pilot Run Report. The various steps involved were reviewed in conjunction with an industrial engineering station capacity study; station capacity data was obtained through an RCA funded time study and covered every aspect of the device fabrication. The time study was reviewed with Dr. Eaton, and proved to be a helpful reference during the demonstration.

Test procedures were also demonstrated. It was verified that the test station design and sequence were adequate to test at a rate of ten good thyristors in an eight hour day.

Figure 1

FLOW DIAGRAM FOR THE TRANSCALENT THYRISTOR ASSEMBLY

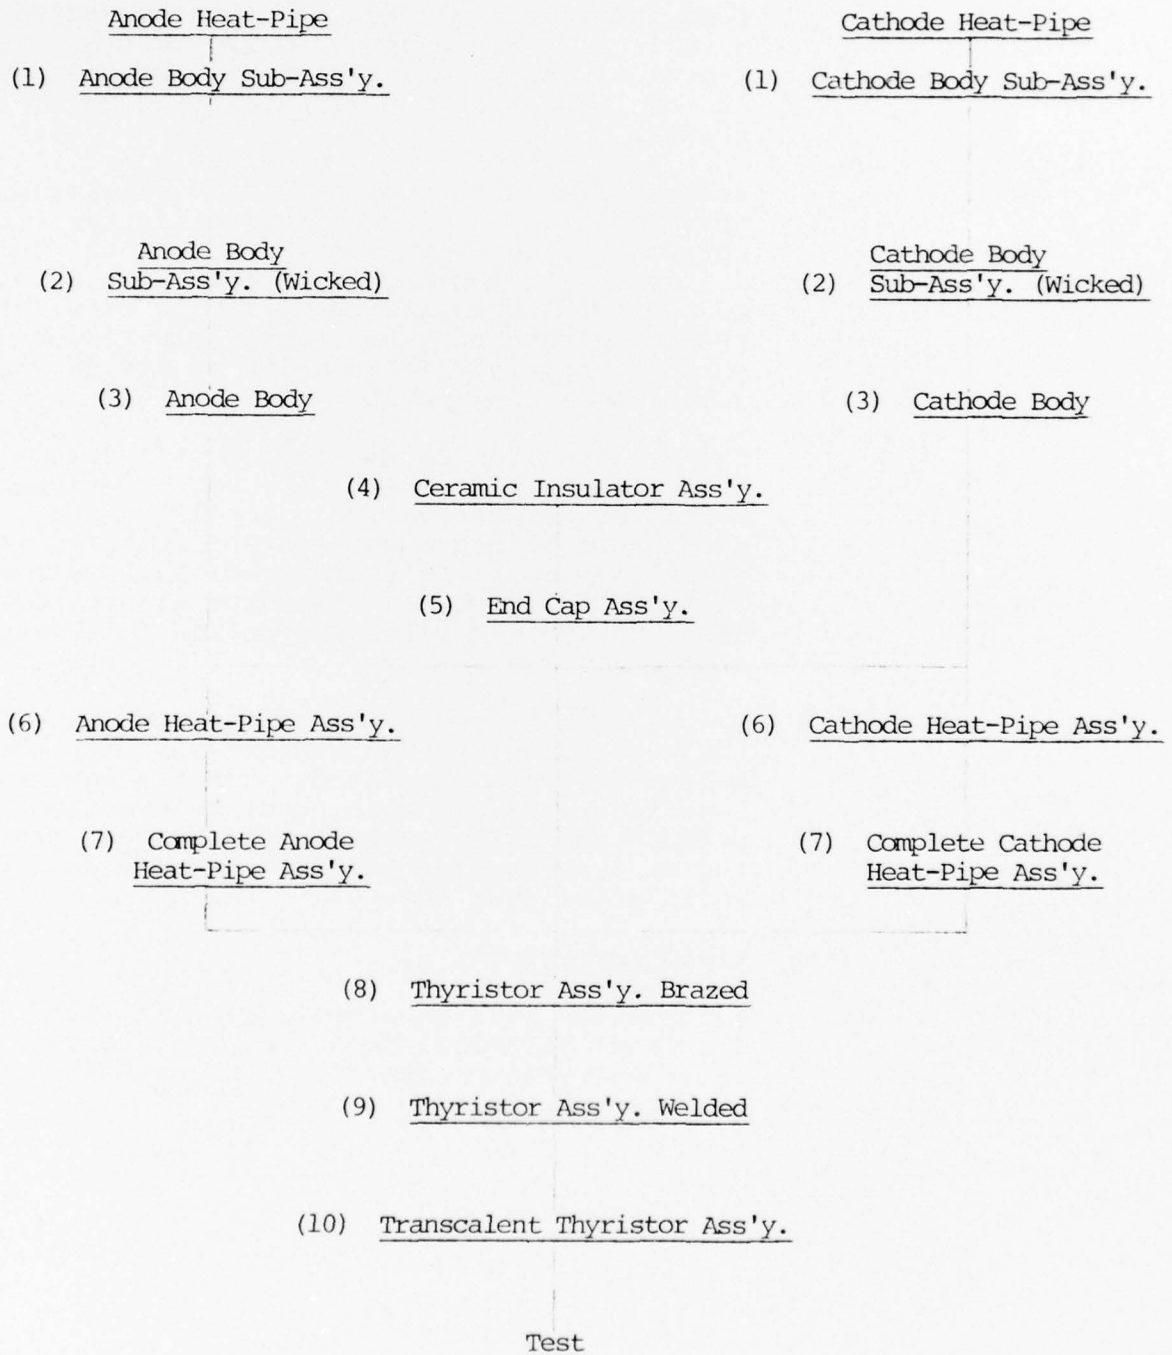

Sufficient parts and sub-assemblies were not available within the scope of the contract to operate every work station at full capacity for an entire shift. Thus the rate verification was performed on a few representative sub-assemblies by the trained operators on the normal work schedule of the first and second shifts. The elapsed time measured for each individual process was then projected to a full eight hour day to verify the rate. Timing of the demonstration was accomplished in this manner in two days covering both shifts.

Brazing fixtures, tools and test equipment of proven design and proven reliability were used throughout the pilot run to produce the units. All purchased and machined parts were inspected to the pertinent drawings prior to utilization. Each manufactured sub-assembly was vacuum-leak checked on a 100% basis prior to its incorporation into a final unit.

The silicon Transcalent thyristor had been incorporated within the contractors' engineering standard, (specification control) system. This meant that part and sub-assembly configurations, as well as, manufacturing processes could be performed against the standards without deviations during the pilot production rate demonstration.

The pilot run demonstration performed for Dr. Eaton verified the contractor's ability through subsequent data presented, such as, engineering specifications and time study information, to produce the J15371 silicon Transcalent thyristor at a production level of ten net good units in an eight hour day.

### iii. Yield Improvement

Information will be prepared and included in the Final Technical Report on the yield improvement accomplished during this MM&TE program.



(b) Item No. 0004AE General Report on Step II

This report for the production planning of the silicon Transcalent thyristor J15371 is being prepared. Draft copies will be submitted to the U.S. Army Mobility Equipment R&D Center for approval. This report will contain a production plan for 80 devices per eight hour day and describe the manpower as well as the facilities to be utilized in the future production of the silicon Transcalent thyristor. Diagrams, tables and time studied rates will be included, per the DD 1423 and the applicable references.

d. Conclusions

The hardware portion of the Pilot Run phase of the contract has been successfully completed by the shipment of the devices on schedule.

Preparations are underway for the completion of the data required, per DD 1423, in the next period.

e. Drawings

Drawings of the piece parts and sub-assemblies of the device were included in the first Quarterly Report with revisions to these engineering drawings subsequently included in the Second Quarterly Report. Subsequent revisions to the heat-pipe strain isolation were included in the Seventh Quarterly Report.

Refer to Table 2 for a cross-reference to the prior technical achievements reported under this contract.

## 2. Process, Equipment and Tooling

### a. Purpose of Each Step

#### (1) Device Processing and Tooling

Figure 4, Engineering Drawing No. 3025577, in the First Quarterly Report, showed the flow of parts through the various assembly steps and a descriptive title was listed for each operation. Also shown were the sub-assembly drawings and fixture drawing numbers for each operation. In both the First and Second Quarterly Reports, the procedures for using the fixtures were included with a photograph of each fixture. This information continued to be used for the device fabrication and processing.

#### (2) Electrical and Environmental Test Equipment

The flow chart of the electrical and environmental testing sequence was given in Figure 7, Drawing No. 3025578, of the First Report. The name of the test was given as well as the special conditions and the MIL-STD-750B method number. Long-time tests had the time interval indicated in the figure. This chart remained valid for the program.

### b,c. Problem Areas and Work to Resolve Problems

#### (1) Device Processing and Tooling

Fabrication processes that were determined to limit the production quantities were improved for the Pilot Run by increasing the yields, by increasing the quantity per operation, by reducing the labor required, by improving the fixtures, and by a more complete documentation of the processes.

#### (a) Heat-Pipe Lapping Mechanization

The successful conclusion of the investigation into the machine lapping of the discs that form the evaporator ends of the heat-pipes was reported previously. Superior flatness and surface finishes were obtained on samples lapped at the machine vendor's plant. The procurement of this equipment has been initiated to eliminate a labor-intensive operation. Delivery is expected in the next period.

(2) Electrical Thermal and Environmental Test Equipment

(a) Test Equipment Calibration Schedules

Electrical test equipment calibration dates were listed in Table 4 of the Fourth Quarterly Report. The schedule established for the recalibration of these equipments on a regular basis was used to recalibrate each equipment in this report period. This call-out continues to occur automatically at four to six months intervals. The calibrations are carried out by the RCA Meter Laboratory Calibration and Standards Department.

Environmental test equipment calibrations in the RCA-Lancaster Environmental Laboratory are also performed at four to six months intervals. The calibration schedule was listed in Table 5 of the Fourth Quarterly Report.

d. Conclusion

The process, equipment and tooling designed, fabricated and used to fabricate and evaluate the engineering and confirmatory sample devices has also been used for fabricating the Pilot Run production. No process, equipment or tooling limitations were apparent during the pilot production phase.

e. Drawings and Photographs of Tooling and Equipment

Copies of the drawings of the special tools and fixtures were included in the First Quarterly Report along with Block Diagrams of the test equipment. Tools and fixtures that were revised were included in the Second Quarterly Report. Photographs of these items were included in both reports. These tools and fixtures were used for the Pilot Run.

Photographs of the electrical test equipment were included in the Third Quarterly Report with text references that described each equipment item. Testing procedures for the electrical test equipment were included in Appendix C of the Second Quarterly Report and in the Appendix of the Third Quarterly Report. These were used for the Pilot Run.

Refer to Table 2 for a cross-reference to the prior technical achievements reported under this contract.



### 3. Flow Chart of Manufacturing Process Yield

Manufacturing process yields were determined during the Pilot Run and will be reported in the Final Technical Report.

### 4. Equipment and Tooling Costs

This information will not be included since such a data requirement is generally not applicable to a Firm Fixed Price Contract on equipment and tooling that is purchased and furnished by the contractor for unrestricted use in fabricating the devices required by the contract or for other government end use. RCA has furnished the equipment and tooling used for this contract with the exception of some of the tools and fixtures. A list of the latter items will be included in the Final Technical Report.

## 5. Data and Analysis

### a. Inspections

#### (1) Pilot Run Devices

The Pilot Run devices included in this report were inspected in accordance with paragraph 4.5, using the sampling plan included in this paragraph of the specification SCS-477. The requirements of paragraphs F.49 of the contract as well as 3.1.6 and 3.1.10 of ECIPPR No. 15 are also being observed. Specification modifications No. P00001, P00002 and P00003 have been included.

The evaluation testing of the initial candidates for the Pilot Run requirement began in April in accordance with the Test Plan submitted previously (SLIN No. 0005AA).

Testing of these devices was finalized in September. Detailed comments, analyses and discussions of those results will be listed in the final technical report (SLIN No. 0004AC).

The test results of forty devices tested for the Pilot Run are summarized in the attached Tables 1. The following codes are utilized in the tables.

Code: P - Passed, including all of the final measurements required after each major test.

IP - Test is in progress.

F - Failed this test.

A - Acceptance judged from another Pilot Run sample submitted to this test; per SCS-477, para. No. 4.5.

PRECEDING PAGE BLANK-NOT FILMED

b. Discussion of Inspection Results

(1) Visual and Mechanical Inspections

Inspection of device No. F35 disclosed a hair-line crack in the high-voltage ceramic and the device, although operable, was considered to be rejected. However, this device passed all of Group A and a portion of the Group B inspections, including the surge test. This device failure along with the dv/dt failure of device No. F43 comprised the two allowed failures at Group A, Sub-Groups 1-4 inspection. Both are operable devices that failed only to meet one limit specified in SCS-477. Both passed several other tests required for the Pilot Run devices, as summarized in Table 1a, below. Both were shipped in fulfillment of the Pilot Run device requirements.

TABLE 1a

SUMMARY OF PILOT RUN DEVICES  
PERFORMANCE vs. SPECIFICATIONS

Inspection	Device Serial No.													
	F33	F35	F36	F39	F40	F41	F42	F43	F46	F49	F50	F51	F52	F54
Group A, Sub-Groups 1-4	P	F	P	P	P	P	P	P	P	P	P	P	P	P
Vis. & Mech.	P	P	P	P	P	P	P	P	P	P	P	P	P	P
i <sub>RBOM</sub> @ 25°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
i <sub>FBOM</sub> @ 25°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
I <sub>H</sub> @ 25°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
i <sub>RBOM</sub> @ 125°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
i <sub>FBOM</sub> @ 125°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
V <sub>GT</sub> @ 25°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
I <sub>GT</sub> @ 25°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
V <sub>GT</sub> @ 125°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
I <sub>GT</sub> @ 125°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
dv/dt @ 125°C	P	P	P	P	P	P	P	F	P	P	P	P	P	P
t <sub>OFF</sub> @ 25°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
V <sub>FM</sub> @ T <sub>C</sub> = 100°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P

TABLE 1a (cont.)

SUMMARY OF PILOT RUN DEVICES  
PERFORMANCE vs. SPECIFICATIONS

Inspection	Device Serial No.												
Group A													
Sub-Groups 1-4													
Vis. & Mech.	P	P	P	P	P	P	P	P	P	P	P	P	P
i <sub>RBOM</sub> @ 25°C	P	P	P	P	P	P	P	P	P	P	P	P	P
i <sub>FBOM</sub> @ 25°C	P	P	P	P	P	P	P	P	P	P	P	P	P
I <sub>H</sub> @ 25°C	P	P	P	P	P	P	P	P	P	P	P	P	P
i <sub>REOM</sub> @ 125°C	P	P	P	P	P	P	P	P	P	P	P	P	P
i <sub>FBOM</sub> @ 125°C	P	P	P	P	P	P	P	P	P	P	P	P	P
V <sub>GT</sub> @ 25°C	P	P	P	P	P	P	P	P	P	P	P	P	P
I <sub>GT</sub> @ 25°C	P	P	P	P	P	P	P	P	P	P	P	P	P
V <sub>GT</sub> @ 125°C	P	P	P	P	P	P	P	P	P	P	P	P	P
I <sub>GT</sub> @ 125°C	P	P	P	P	P	P	P	P	P	P	P	P	P
dv/dt @ 125°C	P	P	P	P	P	P	P	P	P	P	P	P	P
t <sub>OFF</sub> @ 25°C	P	P	P	P	P	P	P	P	P	P	P	P	P
V <sub>FM</sub> @ T <sub>C</sub> = 100°C	P	P	P	P	P	P	P	P	P	P	P	P	P

TABLE 1a (cont.)

SUMMARY OF PILOT RUN DEVICES  
PERFORMANCE vs. SPECIFICATIONS

Inspection	Device Serial No.												
	F79	F80	F82	F84	F85	F86	F87	F88	F91	F92	F95	F98	F100
Group A, Sub-Groups 1-4	P	P	P	P	P	P	P	P	P	P	P	P	P
	P	P	P	P	P	P	P	P	P	P	P	P	P
	P	P	P	P	P	P	P	P	P	P	P	P	P
	P	P	P	P	P	P	P	P	P	P	P	P	P
Vis. & Mech.													
iRBOM @ 25°C													
iRBOM @ 25°C													
I <sub>H</sub> @ 25°C													
iRBOM @ 125°C													
iFBOM @ 125°C													
V <sub>GT</sub> @ 25°C													
I <sub>GT</sub> @ 25°C													
V <sub>GT</sub> @ 125°C													
I <sub>GT</sub> @ 125°C													
dv/dt @ 125°C													
t <sub>OFF</sub> @ 25°C													
V <sub>FM</sub> @ T <sub>C</sub> = 100°C													



TABLE 1b

SUMMARY OF PILOT RUN DEVICES  
PERFORMANCE vs. SPECIFICATIONS

Inspection	Device Serial No.													
	F33	F35	F36	F39	F40	F41	F42	F43	F46	F49	F50	F51	F52	F54
Group B, Sub-Groups 1-4														
$I_{FM}$ (Surge)	A	P	A	A	A	A	P		A	A	A	A	A	A
$\theta_{jc}$ , Initial	P	P	P	P	P	P	P	P	P	P	P	P	P	P
$V_{GT}$ @ -25°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
$I_{GT}$ @ -25°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
$V_{FM}$ @ -25°C	P	P	P	P	P	P	P	P	P	P	P	P	P	P
Thermal Shock	P	A	A	A	A	A	A	A	P	A	A	P	A	A
Moisture Resistance	P	A	A	A	A	A	A	A	P	A	A	A	A	A
Block. V. Life Test @ 125°C	A	A	P	A	A	A	P	A	A	A	A	P	A	A

TABLE 1b (cont.)  
SUMMARY OF PILOT RUN DEVICES  
PERFORMANCE vs. SPECIFICATIONS

Inspection	Device Serial No.												
Group B, Sub-Groups 1-4	F55	F56	F57	F58	F60	F65	F67	F68	F69	F71	F72	F75	F76
$I_{FM}$ (Surge)	A	A	P	A	A	A	A	A	A	A	A	A	A
$\theta_{jc}$ , Initial	P	P	P	P	P	P	P	P	P	P	P	P	P
$V_{GT}$ @ -25°C	P	P	P	P	P	P	P	P	P	P	P	P	P
$I_{GT}$ @ -25°C	P	P	P	P	P	P	P	P	P	P	P	P	P
$V_{FM}$ @ -25°C	P	P	P	P	P	P	P	P	P	P	P	P	P
Thermal Shock	A	A	A	A	A	A	A	A	A	A	A	A	A
Moisture Resistance	A	A	A	A	A	A	A	A	A	A	A	A	A
Block. V. Life Test @ 125°C	A	A	A	A	A	A	P	P	A	A	A	A	A



TABLE 1b (cont.)  
SUMMARY OF PILOT RUN DEVICES  
PERFORMANCE vs. SPECIFICATIONS

Inspection	Device Serial No.												
Group B													
Sub-Groups 1-4													
$I_{FM}$ (Surge)	A	A	P	P	A	A	A	A	A	A	A	A	A
$\theta_{jc}$ , Initial	P	P	P	P	P	P	P	P	P	P	P	P	P
$V_{GT}$ @ -25°C	P	P	P	P	P	P	P	P	P	P	P	P	P
$IG_T$ @ -25°C	P	P	P	P	P	P	P	P	P	P	P	P	P
$V_{FM}$ @ -25°C	P	P	P	P	P	P	P	F	P	F	P	P	P
Thermal Shock	P	P	A	A	A	A	A	A	A	A	A	A	A
Moisture Resistance	P	P	A	A	A	A	A	A	A	A	A	A	A
Block. V. Life Test @ 125°C	A	A	A	A	A	A	A	A	A	A	A	A	A

Table 1c  
SUMMARY OF PILOT RUN DEVICES  
PERFORMANCE vs. SPECIFICATIONS

Inspection	Device Serial No.												
	F33	F35	F36	F39	F40	F41	F42	F46	F49	F50	F51	F52	F54
Group C, Sub-Group 1-5													
Physical Dimen.	P	P	P	P	P	P	P	P	P	P	P	P	P
Shock	A	A	A	A	A	A	A	A	A	P	A	A	A
Vibration	A	A	A	A	A	A	A	A	A	P	A	A	A
Constant Accel.**	A	A	A	A	A	A	A	A	A	A	A	A	A
Barom. Press. Reduced	A	A	A	A	A	A	A	A	P	A	A	A	A
Salt Atmosphere	A	A	A	A	A	P	A	A	A	A	A	A	A
Thermal Fatigue	A	A	A	P	P	A	A	A	A	A	A	A	A
$\theta_{jc}$ , Final	P	A	P	P	P	P	P	P	P	P	P	P	P
Isothermal Charact.	P	P	P	P	P	P	P	P	P	P	P	P	P

\*\*Information only test, per contract paragraph F3, item 7.

TABLE 1c (cont.)  
SUMMARY OF PILOT RUN DEVICES  
PERFORMANCE vs. SPECIFICATIONS

Inspection	Device Serial No.												
Group C, *													
Sub-Groups 1-5													
Physical Dimen.	P	P	P	P	P	P	P	P	P	P	P	P	P
Shock	P	A	A	A	A	P	P	A	A	A	A	A	A
Vibration	P	A	A	A	A	P	P	A	A	A	A	A	A
Constant Accel. **	A	A	A	A	A	A	A	A	A	A	A	A	A
Barom. Press. Reduced	A	A	A	P	A	A	A	A	A	A	A	A	A
Salt Atmosphere	A	P	A	P	P	A	A	A	A	A	A	A	A
Thermal Fatigue	A	A	A	A	P	A	A	P	A	A	A	A	A
$\theta_{jc}$ , Final	P	P	P	P	P	P	P	P	P	P	P	P	P
Isothermal Charact.	P	P	P	P	P	P	P	P	P	P	P	P	P

\*\*Information only test, per contract paragraph F3, item 7.

TABLE 1c (cont.)

SUMMARY OF PILOT RUN DEVICES  
PERFORMANCE vs. SPECIFICATIONS

Inspection	Device Serial No.												
Group C, Sub-Groups 1-5	F79	F80	F82	F84	F85	F86	F87	F88	F91	F92	F95	F98	F100
Physical Dimen.	P	P	P	P	P	P	P	P	P	P	P	P	P
Shock	A	A	A	A	A	A	A	A	A	A	A	A	A
Vibration	A	A	A	A	A	A	A	A	A	A	A	A	A
Constant Accel.**	A	A	A	A	A	A	A	A	A	A	A	A	A
Barom. Press. Reduced	P	P	A	A	A	A	A	A	A	A	A	A	A
Salt Atmosphere	A	A	A	A	A	A	A	A	A	A	A	A	A
Thermal Fatigue	A	A	A	A	A	A	A	A	A	A	A	A	A
$\theta_{jc}$ , Final	P	P	P	P	P	P	P	P	P	P	P	P	P
Isothermal Charact.	P	P	P	P	P	P	P	P	P	P	P	P	P

\*\*Information only test, per contract paragraph F3, item 7.

c. Corrective Action

Previously reported corrective actions have proven successful in securing a reproducible thyristor device with consistently good electrical, thermal, mechanical and environmental characteristics. The results listed above for the pilot run are believed to verify this conclusion.

## 6. Specification

There are no further modifications proposed for the specification No. SCS-477. RCA has verified in the Pilot Run that the Transcendent thyristors fabricated during this phase of the contract meet all of the requirements of the specification.

## 7. Requirement for Pilot Run

The space, manpower, facilities, tooling, etc., required for the Pilot Run were listed in the Preliminary Pilot Run Report, dated 30 May 1978, and submitted separately as Contract Data Item No. 0004AE.

## 8. Total Cost for Pilot Run

Cost data will become available when the Pilot Run is completed. The total cost of the Pilot run phase through this quarterly period is almost \$55,000.00 for the materials, labor and overhead costs, but prior to the addition of any general and administrative expenses or fees. Over six percent of the total represents the material costs.

These expenditures, although not quite complete, are less than the estimated costs for the Pilot Run phase because of the additional preparatory work performed in the prior phases as well as the utilization of some parts and materials purchased previously for the total contract scope.

## 9. Program Review

The PERT Chart revision submitted 29 August 1977 remains in effect with the Pilot Run delivery made on schedule in late September, 1978. The final program data is expected to be submitted also on schedule.



## CONCLUSIONS

Effort expended in the eighth contract quarter was successful in finishing the Pilot Run Samples. Verification on the Confirmatory Samples that the design had met all of the specifications added assurance that the Pilot Run phase would also be successful. Time studies have been used to verify the required production rate capability exists on the work stations. Where required, increases in capacity were made at the few limiting work stations, to bring them up to the required pilot production rate. RCA is thus confident in having met the full MM&TE specification requirements for the Pilot Run devices. Both improved wafers and improved packages were fabricated for these devices.

The program has proceeded in accordance with the latest revised PERT Chart, dated 29 August 1977. All of the Pilot Run devices have been completed and shipped, to date.

PRECEDING PAGE BLANK-NOT FILMED

PROGRAM FOR THE NEXT PERIOD

1. Issue the final monthly reports,
2. Submit the draft copies of this Eighth Quarterly Report for government approval,
3. Prepare and submit the draft copies of the General Report on Step II for government approval, and
4. Prepare and submit the draft copies of the Final Technical Report for government approval.



#### IDENTIFICATION OF PERSONNEL

The professional and skilled technical personnel who are actually working on the MM&TE project during the first eight quarters of the contract have varied backgrounds, as listed in the biographical resumes included in the previous Quarterly Reports. However, additional resumes are included in this report since added personnel were assigned to the project in the eighth quarter.

In addition to the major responsibilities, above, numerous supporting personnel including managers, secretaries, purchasing agents, environmental technicians, machinists, electricians, experimental tube builders, etc., have contributed to the progress made in the first twenty-four months of the contract.

Patrick M. Bransby - Electronics Technician, Electrical and  
Mechanical

Mr. Bransby graduated from Columbia High School and Willow Street Vocational Technical School in 1978 where he majored in Electronics. He joined the Transcalent Development group in August of the same year.

The subjects taken at Willow Street during his two years of study included Basic Electric Theory, Vacuum Tube Theory, Solid State Circuits, Practical Amplifier Circuits and courses on the operation of oscilloscopes, power supplies, meters and other laboratory equipment.

Since he joined the Transcalent group in August, Mr. Bransby has acquired additional skills, such as the evaluation of solid state MM&T devices through DV/DT, thermal impedance, on-state voltage and many other tests.

At the present time, he is continuing his theoretical education through RCA's Engineering Technology Program. He will be assigned to the inspection phase of the proposed Transcalent contract.

Wendy L. Krown - Publications' Technician

Miss Krown graduated from Manheim Twp. H.S. and Susquehanna University in 1974 and 1978, respectively. She earned a B.A. degree in English and a B.A. degree in Theater. She has recently joined the Transcalent Engineering group as the Publications' Technician with responsibilities for editing and writing the numerous reports required by this and other government contracts.

Applicable subjects taken in the schools, above, included Organic and Inorganic Chemistry, General Physics, Advanced Biology, and Advanced English courses. Her studies also included courses in Expository Writing, Creative Writing, many and varied literature courses, and Interpersonal Communications, as well as Broadcasting, where she qualified for the FCC Third Class Operator's License. She furthered her science background by electing additional courses in Biology and Geology as well as technical mathematics courses.

#### DISTRIBUTION LIST

The following pages include the distribution list supplied by the contracting officer with the approval letter for the First Quarterly Report as well as the additions authorized subsequently.

That list was utilized also for the distribution of the Second, Third, Fourth and Fifth Quarterly Reports. One deletion was made for the Sixth and Seventh Quarterly Reports. Additional revisions were made for the Eighth Quarterly Report, however, no new corrections were made for this Final Technical Report.

# DISTRIBUTION OUTSIDE OF RCA-SSD

Dr. Paul E. Greene  
Dir. Solid State Lab.  
Hewlett Packard Co.  
1501 Page Mill Road  
Palo Alto, CA 94304

Mr. Gerald B. Herzog  
Staff Vice President  
Technology Centers  
RCA  
David Sarnoff Res. Ctr.  
Princeton, NJ 08540

Dr. George E. Smith  
Bell Telephone Labs, Inc.  
MOS Device Dept.  
600 Mountain Ave.  
Room 2A323  
Murray Hill, NJ 07974

Commander  
U.S. Army Electronics Command  
ATTN: DRSEL-TL-1  
Mr. Robert A. Gerhold  
Fort Monmouth, NJ 07703

Commander  
Harry Diamond Labs.  
2800 Powder Mill Rd.  
ATTN: DRXDO-RCC,  
Mr. Anthony J. Baba  
Adelphi, MD 20783

Commanding Officer  
Picatinny Arsenal  
ATTN: SARPA-ND-D-A-4  
Mr. Arthur H. Hendrickson  
Bldg. 95  
Dover, NJ 07801

Commanding General  
U.S. Army Missile Command  
ATTN: Mr. Victor Ruwe,  
DRSMI-RGP  
Redstone Arsenal, AL 35809

Commander  
U.S. Army Electronics Command  
ATTN: DRSEL-TL-BS  
Mr. George W. Taylor  
Fort Monmouth, NJ 07703

Commanding Officer  
U.S. Army Research Office  
P.O. Box 12211  
ATTN: Dr. Chas. Boghosian  
Research Triangle Park, NC 27709

Naval Research Laboratory  
ATTN: Dr. David F. Barbe,  
Code 5260  
4555 Overlook Avenue, SW  
Washington, DC 20375

Naval Electronics Lab Center  
ATTN: Mr. Charles E. Holland, Jr.  
Code 4300  
271 Catalina Blvd.  
San Diego, CA 92152

The Johns Hopkins Univ.  
Applied Physics Laboratory  
ATTN: Dr. Charles Feldman  
11100 Johns Hopkins Road  
Laurel, MD 20810

Commander  
Naval Surface Weapons Center  
ATTN: Mr. Albert D. Krall,  
Code WR-43  
White Oak  
Silver Spring, MD 20910

Commander  
RADC  
ATTN: Mr. Joseph B. Brauer, RBRM  
Griffiss AFB, NY 13441

NASA  
Geo. C. Marshall Space Flight Center  
ATTN: Dr. Alvis M. Holladay, Code EC-41  
Marshall Space Flight Center, AL 35812

NASA  
Langley Research Center  
Langley Station  
ATTN: Mr. Charles Husson, M/S 470  
Hampton, VA 23665

Dir. National Security Agency  
ATTN: Mr. John C. Davis, R55  
Fort George C. Meade, MD 20755



Commander  
U.S. Army Production  
Equipment Agency  
ATTN: AMXPE-MT  
(Mr. C. E. McBurney)  
Rock Island, IL 61201

Mr. Jack S. Kilby  
5924 Royal Lane  
Suite 150  
Dallas, TX 75230

Dr. Barry Dunbridge  
TRW Systems Group  
One Space Park  
Redondo Beach, CA 90278

Mr. Harold D. Toombs  
Texas Instruments, Inc.  
P.O. Box 5474; M/S 72  
Dallas, TX 75222

Commander, AFAL  
ATTN: AFAL/DEH  
Mr. Stanley E. Wagner  
Wright Patterson AFB,  
OH 45433

Lincoln Laboratory, MIT  
ATTN: Dr. Donald J. Eckl  
P.O. Box 73  
Lexington, MA 02173

RADC (ETSD)  
ATTN: Mr. Sven Roosild  
Hanscom AFB, MA 01731

General Electric Company  
Semi-Conductor Products Dept.  
Building 7, Box 42  
Syracuse, NY 13201

Micro-Electronics Laboratory  
Hughes Aircraft Company  
500 Superior Avenue  
Newport Beach, CA 92663

Silicon Transistor Corp.  
ATTN: Mr. P. Fitzgerald  
Katrina Road  
Chelmsford, MA 01824

Mr. Daniel Becker  
Reliability & Qual. Test Center  
Mannes Spacecraft Center  
Houston, TX 77058

Texas Instruments, Inc.  
Library M.S. 20  
P.O. Box 5012  
Dallas, TX 75222

Dr. S. Bakalar  
Transitron Electronic Corp.  
168 Albion Street  
Wakefield, MA 01880

Mr. R. Riel  
Westinghouse Electric Corp.  
R&D Center  
Pittsburgh, PA 15235

Solitron Devices  
256 Oak Tree Road  
Tappan, NY 10983

Dr. L. Suelzle  
Delta Electronics Corp.  
2801 S. E. Main Street  
Irvine, CA 92714

Bell Laboratories  
ATTN: Mr. B. H. Hamilton  
Whippany Road  
Whippany, NJ 07981

Commander  
Naval Ships Res. & Dev. Center  
ATTN: W. Kohl (Bldg. 100-3)  
Annapolis, MD 21402

Power Systems Division  
ATTN: Mr. Kenneth Lipman  
Box 109  
South Windsor, CT 06074

Martin Marietta  
ATTN: Mr. E. E. Buchanan  
P.O. Box 179  
Denver, CO 80201



J. J. Henry Co., Inc. Special Proj.  
Attn: Mr. Mike Saboe - NSRDC Study  
Suite 838  
2341 Jefferson Davis Highway  
Arlington, VA 22202

Fermi National Accelerator Lab.  
ATTN: Mr. Frank S. Cilyo  
P.O. Box 500  
Batavia, IL 60510

Hughes Aircraft Company  
Ground Systems Group  
ATTN: Dr. Kal Sekhon  
Fullerton, CA 92634

Commander  
Navy Weapons Center  
ATTN: Mr. S. S. Lafon  
China Lake, CA 93555

Commander (2)  
U.S. Army Electronics Command  
ATTN: DRSEL-PP-I-PI  
Mr. William R. Peltz  
Fort Monmouth, NJ 07703

Commander (2)  
U. S. Army Mobility Equipment  
Research and Development Ctr.  
ATTN: DRD ME-EA  
Mr. Ted Perkins  
Fort Belvoir, VA 22060

Advisory Group on Electron Dev. (2)  
ATTN: Working Group on Pwr. Devices  
201 Varick Street  
New York, NY 10014

Mr. Ron Wade  
ATTN: ELEX-0151431  
Naval Electronic Sys. Command  
Washington, DC 20360

Dr. Robert Redicker  
Mass. Inst. of Technology (MIT)  
Building 13-3050  
Cambridge, MA 02139

Defense Electronics Supply Ctr.  
Directorate of Engineering  
and Standardization  
DESC-ECS (Mr. N. Hauck)  
1507 Wilmington Pike  
Dayton, OH 45401

General Instrument Corp.  
Semi-Conductor Prod. Group  
ATTN: Mr. G. Cohen  
600 W. John Street  
Hicksville, LI, NY 11802

Harry Diamond Laboratories  
ATTN: Technical Library  
Connecticut Avenue and  
Van Ness Street  
Washington, DC 20438

Jet Propulsion Laboratory  
ATTN: Mr. L. Wright  
Mail Stop 158-205  
4800 Oak Grove Drive  
Pasadena, CA 71103

NASA  
Lewis Research Center  
ATTN: Mr. Gail Sundberg (MS54-4)  
2100 Brook Park Road  
Cleveland, OH 44135

Commander  
AF Aero Propulsion Lab.  
ATTN: AFAL/PODI  
(Mr. Philip Herron)  
Wright Patterson AFB OH 45433

Commander  
Naval Air Development Center  
ATTN: Mr. Howard Ireland (3043)  
Mr. Joseph Segrest  
Warminster, PA 18974

Commander  
NAVSEC Code 420 CTRBG  
ATTN: Mr. Arnold D. Hitt, Jr.  
801 Center Building  
Hyattsville, MD 20782

Delco Electronics  
ATTN: Dr. A. Barrett  
Mail Code 8106  
676 Hollister Avenue  
Goleta, CA 93017

NASA  
Johnson Space Center  
ATTN: Mr. E. Wood, Code EG2  
Houston, TX 77058

Garrett Air Research Mfg. Co.  
of Arizona  
ATTN: Mr. R. N. McGinley  
P.O. Box 5217  
402 S. 36th Street  
Phoenix, AZ 85010

Lockheed California Co.  
ATTN: Mr. W. W. Cloud  
Department 75-82  
Bldg. 63/3, Box 551  
Plant A-1  
Burbank, CA 91520

Sanders Associates  
ATTN: Mr. A. Hurley  
NCAI - 6247  
95 Canal Street  
Nashua, NH 03061

Defense Documentation Center (12)  
ATTN: DDC-IRS  
5010 Duke Street  
Cameron Station (Bldg. 5)  
Alexandria, VA 22314

NASA  
Scientific & Tech. Inf. Off./KSI  
Washington, DC 20541

Commander  
U.S. Army Electronics Command  
Communications Systems  
Procurement Branch  
Fort Monmouth, NJ 07703  
ATTN: Capt. H. John Patch/PCO  
DRSEL-PP-C-CS-1

TRW, Inc.  
Defense & Space Systems Group  
ATTN: Mr. Art Schoenfeld  
One Space Park  
Redondo Beach, CA 90278

Garrett Air Research  
ATTN: Mr. Everett Geis  
2525 West 190 Street  
Torrance, CA 90509

Airesearch Manufacturing Co.  
ATTN: Mr. John Ashmore  
Electronic Systems  
2525 W. 190th Street  
Torrance, CA 90509

Naval Underwater Systems Center  
ATTN: Mr. George Anderson/Code 3642  
Newport, RI 02840

Dr. Roy Scott Hickman  
Chairman, Dept. of Mech.  
and Environ. Engrg.  
University of California  
Santa Barbara, CA 93106

# DISTRIBUTION WITHIN RCA-SSD

Dr. R. E. Simon 055-191	H. F. Lebegern 068-682
C. W. Bizal 057-631	Library 686
W. S. Lynch 057-631	R. M. Bowes 057-631
E. D. Fleckenstein 053-460	J. G. Kindbom/W. Peppler 003-953
N. R. Hangen (2) 073-637	P. Harvest 087 963
S. W. Kessler 086-963	J. V. Platt Somerville
D. R. Trout 086-963	C. Turner Somerville
W. T. Burkins 086-963	K. C. Harding Arlington
C. V. Reddig 086-963	E. Schmitt Somerville
A. J. Witkowski 086-963	B. B. Adams 086-963
R. M. Hopkins 086-963	J. D. Schmitt 057-634
R. E. Reed (10) 086-963	W. L. Krown 086-963
R. Glicksman - Somerville	
E. D. Savoye 073-632	
T. Edwards/F. Wallace 089-980	
J. Grosh/R. Bauder 080-923	
G. J. Buchko/R. Beam 003-953	
R. F. Keller 086-963	

TABLE 2

SCHEDULE OF PRIOR TECHNICAL  
ACHIEVEMENTS REPORTED UNDER CONTRACT

<u>Quarterly Report Reference</u>		
<u>Description</u>	<u>Issue</u>	<u>Page No.</u>
I. <u>Engineering Sample Phase:</u>		
<u>Drawings and Diagrams</u>		
Assembly Flow-Chart	First	25
Cross-Section of Transcendent Thyristor Chip	Fourth	20
Dimensional Cross-Section Drawing of J15371	Second	14
Functional Block Diagrams for Electrical Test Equipment	First	C1
Inspection Flow Chart	First	29
Parts and Assembly Drawings	First	A1
Parts and Assembly Drawings - Revised	Second	A1
Tooling and Photomask Drawings	First	B1
Tooling and Photomask Drawings - Revised	Second	B1
PERT - Initial	First	67
PERT - Revisions	(Issued separately)	
<u>Graphs</u>		
Case Temperature vs. Average Current	Second	60
Correlation of Holding Current and Turn-Off Time	Third	47
Correlation of Holding Current and On-State Voltage	Third	48
Exponential Rate Voltage Rise Test Circuit Diagram	Second	42
One-Shot Surge Current Circuit	Second	47
Peak On-State Voltage vs. Average Current	Second	58
Thermal Resistance vs. Dissipation	Second	61

TABLE 2 (Cont.)

<u>Description</u>	<u>Quarterly Report Reference</u>	
	<u>Issue</u>	<u>Page No.</u>
<u>Narrative</u>		
Conversion of Design for Production	First	13
Conversion of Design for Production	Second	13
Conversion of Design for Production	Third	13
Conversion of Design for Production	Fourth	13
Data and Analysis	Second	53
Data and Analysis	Third	41
Data and Analysis	Fourth	43
Description of the Structure	First	9
Exponential Rate of Voltage Rise Discussion	Fourth	15
Process, Equipment and Tooling	First	23
Process, Equipment and Tooling	Second	19
Process, Equipment and Tooling	Third	17
Process, Equipment and Tooling	Fourth	29
Test Procedures	Second	C1
Test Procedures	Third	A1
<u>Photographs</u>		
Assembly and Brazing Fixture	First	Fig. 9-13
Assembly and Brazing Fixture	Second	Fig. 3-10
Electrical Test Equipment	Third	Fig. 3-12



TABLE 2 (Cont.)

	<u>Quarterly Report Reference</u>	
<u>Description</u>	<u>Issue</u>	<u>Page No.</u>
<u>Tables</u>		
Electrical Test Equipment Calibration Sched.	Fourth	36
Electrical Test Equipment Inspection Sched.	Second	40
Electrical Test Equipment Survey	Second	30
Environmental Test Equipment Calibration Sched.	Fourth	38
Selection of Five Samples for Delivery	Fourth	50
Summary of Engineering Samples Performance	Fourth	56
Test Data Record Forms - Engineering Sample Devices	Fourth	44
<u>Other References</u>		
Conclusions - Engineering Phase	Fourth	61
Test Report - Silicon Transcendent Thyristor Type J15371	(Issued Separately)	
<u>Confirmatory Sample Phase:</u>		
<u>Diagram</u>		
Technical Organization Chart	Fifth	54
<u>Graphs</u>		
dv/dt vs. Gate Current	Sixth	17
dv/dt vs. Shunt Current	Sixth	16
Forward Blocking Current vs. Case Temperature	Sixth	34
Gate Current vs. Shunt Current	Sixth	15
Gate Trigger Current vs. Case Temperature	Sixth	36
Gate Trigger Voltage vs. Case Temperature	Sixth	37
Histograms - Dimensions	Sixth	42, 43



TABLE 2 (Cont.)

<u>Description</u>	<u>Quarterly Report Reference</u>	
	<u>Issue</u>	<u>Page. No.</u>
Histograms - $I_H$ , $dv/dt$ , $t_{off}$ and $V_{FM}$	Sixth	38
Histograms - $\theta_{JC}$	Sixth	41
Instantaneous Forward Voltage and Current Characteristics	Fifth	44
Isothermal Characteristics	Fifth	44
Reverse Blocking Current vs. Case Temperature	Sixth	35
Thermal Impedance	Fifth	47
Transcendent Package Tensile & Bending Moment Tests	Fifth	Fig. 1-4
<u>Narrative</u>		
Conversion of Design for Production	Fifth	13
Conversion of Design for Production	Sixth	13
Data and Analysis	Fifth	35
Data and Analysis	Sixth	29
Process, Equipment and Tooling	Fifth	27
Process, Equipment and Tooling	Sixth	25
<u>Table</u>		
Test Data - Confirmatory Samples	Sixth	30
<u>Other References</u>		
Conclusions - Confirmatory Phase	Sixth	49
Preliminary Pilot Run Report	(Issued Separately)	
Test Report - Silicon Transcendent Thyristor Type J15371	(Issued Separately)	

TABLE 2 (Cont.)

<u>Description</u>	<u>Issue</u>	<u>Quarterly Report Reference</u>
III. <u>Pilot Run Phase:</u>		
(Refer to Seventh Quarterly and Subsequent Reports)		
